

Status (16 May 2024) Picayune Strand Restoration Project

Roads (99%) and Logging
Trams (100%) Degraded

Canals 70% Plugged

Prairie Canal – 7 Miles

Merritt Canal – 9 Miles

Stair-Step Canal – 5 Miles

Faka Union Canal – 8.4 Miles

3 Pump Stations Built


Remaining Work

Construct Southwest
Protection Features 2024*

Degrade Miller Blvd 2025*

Plug Canals

Miller Canal – 12 Miles 2025*

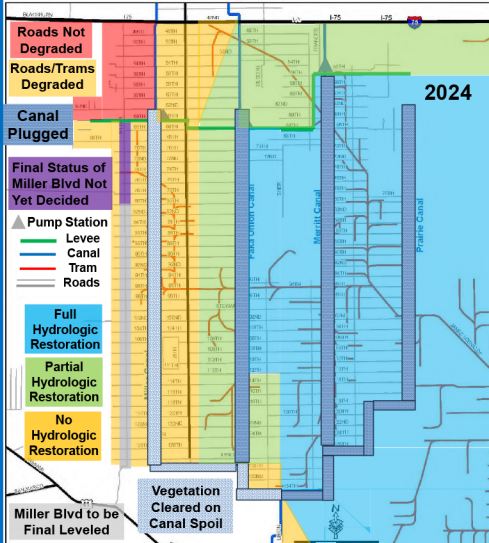

* Currently Under Construction
